



**MOCA**

# Capitol Oversight Group Meeting

October 9, 2019



# Meeting Agenda



*Capitol Rotunda*



## **Overall Project Items**

- a. Landscape update
- b. AV and security camera update
- c. Consolidated Capitol plan update
- d. Building Stewardship guideline



## **Capitol Design and Construction**

- a. Furniture procurement update
  - a. Capitol & Extension furniture
  - b. Custom furniture and lighting



## **Overall Project Items**

- a. Auditorium, Learning Center, and Visitor Center update



## **Public Comment**

# Grand Opening July 10, 2019



# Landscape Update

## Timeline on landscape

- Landscape was delayed due to a wet spring.
- Snowmelt was a scope change and added time.
- Site wall modifications were a scope change.
- Completion = October 31, 2019



# AV and Security Camera Update

---

## **AV Update**

- Hearing Rooms W110 & W113 – October 31, 2019
- JAC – completed by November 2019
- Supreme Court – completed mid to end of December 2019
- Ceremonial Room – completed end of November 2019
- House Chamber – completed first week of December 2019
- Senate Chamber - completed end of December 2019
- Conference Rooms - January 2020
- Herschler Public Meeting Rooms – January 2020

*The above is only for the installation portion.*

- *K2 will work closely with Ford AV to test, commission and punch all rooms.*
- *K2 will coordinate with Ford on their anticipated completion dates in order to install the network switches, configured and do all final programming.*

# AV and Security Camera Update

---

## Security Update

- Security Operation Center (SOC)
  - *Ready for use in about 7 to 8 weeks*
  - *Equipment has been ordered*
- Access control
  - *Live and operational in the Capitol*
  - *Will be live in Herschler next week*
- Cameras
  - *Live and operational in the Capitol*
  - *Extension cameras will come on line with the SOC*


# Consolidated Capitol Plan – Capitol Square

## Consolidated Capitol Plan Progress

The Consolidated Capitol Plan to be complete by end of November 2019

Plan elements to be finalized:

- Remaining statuary on Capitol grounds
- Master Artwork Plan – Consider composites in the public meeting rooms in the Extension.

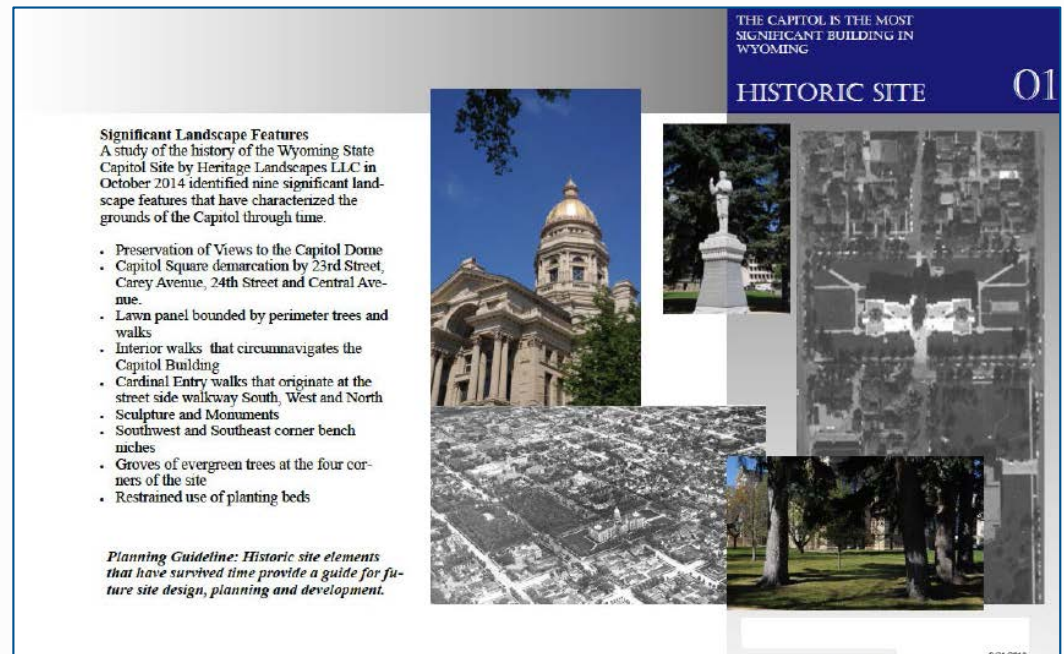

# Consolidated Capitol Plan – Arrival Sequence

THE CAPITOL IS THE MOST  
SIGNIFICANT BUILDING IN  
WYOMING

BUS DROP OFF


16

## Bus Drop Off

School Bus drop off areas should provide an environment that is safe for students and provides a relatively direct path to the Visitor Information and Learning Center located in the Capitol Extension below the Herschler Building and Plaza.

Tour Bus drop off should occur in the same location. Circulation into the site from 25th Street should be restricted for this purpose. A loading zone for automobiles and ADA drop off should also be located in this area. Parking at this area should be removed to accommodate these safe loading and unloading zones.

*Design Guideline: Accommodation should be made for tour and school bus drop off and waiting. Drop off should occur North of the Herschler to provide direct entry into the Visitor Services portion of the Connector.*

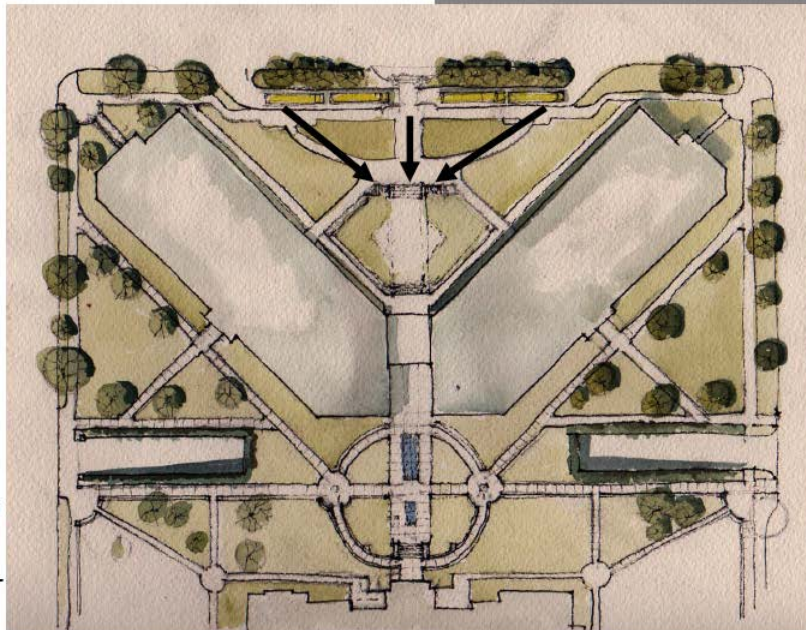

11/30/2015

WORKING DRAFT

# Consolidated Capitol Plan

## Capitol Visitor Center

### Sequence

- Students will arrive at the bus unloading and loading zone North of the Capitol.
- They will immediately move indoors to the Visitor Center in the Extension.
- They will be greeted by Esther Hobart Morris and Chief Washakie at the entry to the Visitor Center and Learning Center.

### Interpretative Plan

#### Extension Gallery Planning Guideline 18

*“Capitol Extension Gallery should be used for sculptures and paintings of enduring and interpretative importance to inspire and support learning at the Wyoming State Capitol”*



# Consolidated Capitol Plan

## Art Locations

- Art Plan – Condition Assessment
- The decision to move sculpture indoor included the analysis and recommendation by the Museum
  - Esther Hobart Morris
  - Chief Washakie

### Note:

Esther, while outside, was hit by a car and damaged.

The Chief as been damaged by theft of feathers. Both statues are fragile and need to be in a more protected environment.



# Consolidated Capitol Plan

## Existing Sculpture Locations

- Future monuments on Capitol Square
- Location of existing monuments

THE CAPITOL IS THE MOST  
SIGNIFICANT BUILDING IN  
WYOMING

MONUMENTS 17

**Monuments and Sculpture**

Commemorative monuments and sculpture are often present on State Capitol Complexes throughout the country. Often these monuments change location over time and new elements are added. The Wyoming State Capitol Grounds are no exception. Many of the elements on the grounds are not in the original location of placement.

The double block occupied by the Capitol is very small and not capable of supporting all sculpture and monuments.

Provisions for adding sculpture and commemorative monuments in the future should also be part of the comprehensive planning process.

Placement of monuments and sculpture should enhance the overall experience of the Capitol Complex and reinforce the planning guidelines of the Consolidated Capitol Plan.

*Planning Guideline: Location of sculpture and other monuments should be carefully planned and accommodation made for possible future monuments. Site Sculpture and Monuments should be located adjacent to but not directly in site axis pathways. Contemplative viewing areas with benches and shade should be provided.*



6/21/2018

# Building Stewardship Guidelines

---

## **Building Stewardship Guidelines include:**

- New wood finish treatment
- Existing wood finish treatment
- New brass elevator finish treatment
- Light fixture finish treatment
- Marble floor finish treatment
- Decorative paint finish treatment and care
- Others

# Furniture Procurement Update

## Capitol and Extension Furniture

- Office Furniture
  - Bids have been received
  - Requested mockup to review design/quality
  - Selection pending
  - Anticipated delivery 8 to 10 weeks after award
- Chair Fair
  - Bid have been received
  - Chairs will be sent for mockup
  - Anticipated delivery in 6 to 8 weeks
- Seating, Café Tables, Upholstered Furniture
  - Selections have been identified
  - CMD to issue purchase orders
  - Delivery to be in 8 to 10 week from order



# Furniture Procurement Update

## Custom Furniture and Lighting

- Custom Furniture
  - Has been designed and approved
  - Has been ordered
  - Shop drawing have been reviewed and approved
  - Changes requested after shop drawings were incorporated
  - Production and manufacturing is underway
  - First delivery prior to November 1, 2019 – Governor's Office and Elected Official's desks
  - Second delivery prior to December 1, 2019 – Remaining custom furniture



# Furniture Procurement Update





---

- **Custom Lamps – Supreme Court and Chambers**
  - Chamber lamps have been completed.
  - Supreme Court Torchieres are assembled presently being finished.
  - Will ship October 16, 2019



# Furniture Procurement Update

|      |                        | Tables<br>w/Power | Tables No<br>Power | Very<br>Chairs |
|------|------------------------|-------------------|--------------------|----------------|
| E034 | Capitol Club           |                   | 10                 | 20             |
| W053 | Conference Room        | 10                | 8                  | 90             |
| W054 | Conference Room        | 15                |                    | 80             |
| W052 | Conference Room        | 5                 | 5                  | 25             |
| W056 | Conference Room        | 6                 |                    | 15             |
|      |                        |                   |                    |                |
| W001 | Sm Public Meeting Room | 11                |                    | 55             |
| W002 | Sm Public Meeting Room | 11                |                    | 55             |
| W003 | Sm Public Meeting Room | 11                |                    | 65             |
| W004 | Sm Public Meeting Room | 11                |                    | 50             |
| W005 | Lg Public Meeting Room | 15                |                    | 100            |
| W006 | Lg Public Meeting Room | 10                | 3                  | 75             |
|      |                        |                   |                    |                |
|      |                        |                   |                    |                |
| WG42 | Conference Room        | 6                 |                    |                |
| EG36 | Policy Conference Room | 6                 |                    |                |
| EG34 | Conference Room        | 4                 |                    |                |
|      |                        |                   |                    |                |
|      |                        | 121               | 3                  | 630            |

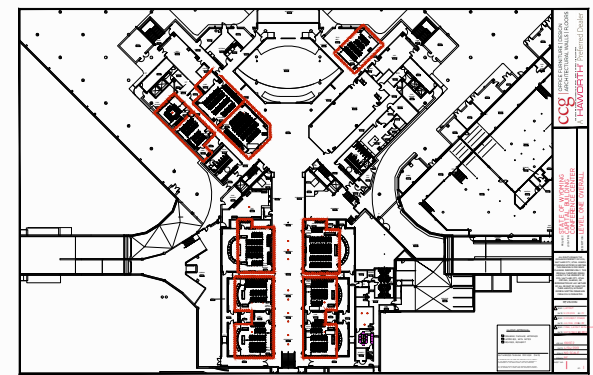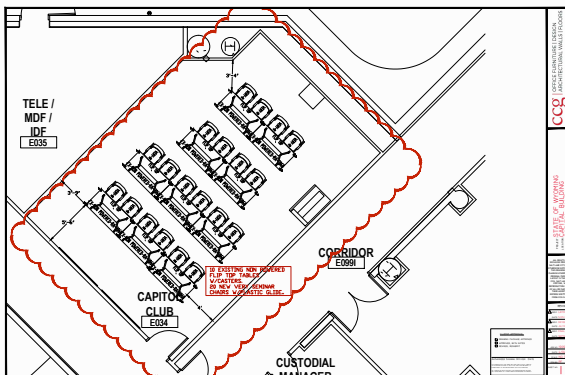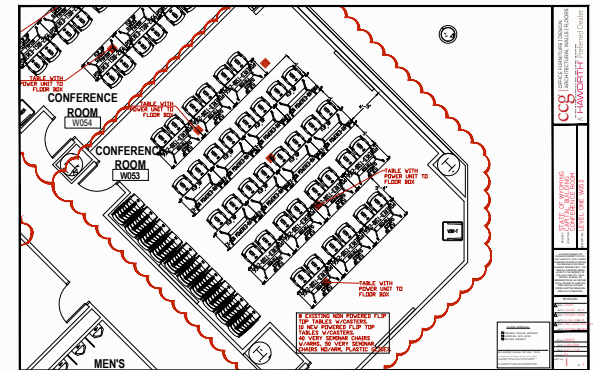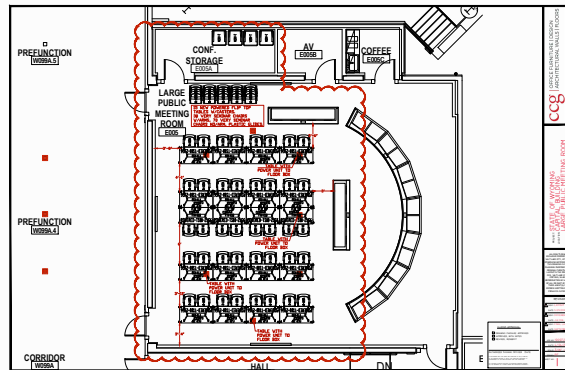

# Auditorium, Learning Center & Visitor Center

---

## Construction Update

- Permits have been issued
- Procurement of materials has occurred
- Work is underway
- Substantial Completion January 31, 2020.

